


Act ID	Activity Description	RESP	Orig Dur	Remaining Duration	Early Start	Early Finish	Total Float	2009												2010												2011											
								AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL												
<b>27JUL09</b>																																											
1000	Contract Award		0	0	28JUL09	27JAN11	0	Contract Award																																			
2041	Maintain SC-10		382d	382d *	28JUL09	27JAN11	0	Maintain SC-10																																			
2043	Install and Maintain SC-6		382d	382d *	28JUL09	27JAN11	0	Install and Maintain SC-6																																			
2083	Maintain SS-7		382d	382d *	28JUL09	27JAN11	0	Maintain SS-7																																			
2093	Install and Maintain SS-9 (Bioswale)		382d	382d *	28JUL09	27JAN11	0	Install and Maintain SS-9 (Bioswale)																																			
<b>17AUG09</b>																																											
1010	Contract Approval		1d	1d	20AUG09	20AUG09	0	Contract Approval																																			
1040	Develop SWPPP		5d	5d	21AUG09	27AUG09	10d	Develop SWPPP																																			
1020	Create CPM Schedule		8d	8d	21AUG09	01SEP09	16d	Create CPM Schedule																																			
1270	Lead Excavation and Transportation Plan Devel		9d	9d	21AUG09	02SEP09	147d	Lead Excavation and Transportation Plan Devel																																			
1250	Lead Compliance Plan Creation		10d	10d	21AUG09	03SEP09	144d	Lead Compliance Plan Creation																																			
1055	Notice of materials to be used		20d	20d	21AUG09	18SEP09	15d	Notice of materials to be used																																			
1060	Sign Panel Statement of Order		20d	20d	21AUG09	18SEP09	15d	Sign Panel Statement of Order																																			
1070	Irrigation Breakdown		20d	20d	21AUG09	18SEP09	15d	Irrigation Breakdown																																			
1075	Statement of Plant Order		20d	20d	21AUG09	18SEP09	15d	Statement of Plant Order																																			
1080	Bird Nesting Survey		20d	20d	21AUG09	18SEP09	15d	Bird Nesting Survey																																			
1090	Notice of Order Electrical Mateial		20d	20d	21AUG09	18SEP09	15d	Notice of Order Electrical Mateial																																			
1100	Communications Routing Material		20d	20d	21AUG09	18SEP09	5d	Communications Routing Material																																			
1120	Statement of Sign Panel Order		20d	20d	21AUG09	18SEP09	15d	Statement of Sign Panel Order																																			
1130	Traffic Control Contingency Plan		20d	20d	21AUG09	18SEP09	15d	Traffic Control Contingency Plan																																			
1140	Notice of Order Structral Steel		20d	20d	21AUG09	18SEP09	15d	Notice of Order Structral Steel																																			
1190	Rapid Set PCC QCP		20d	20d	21AUG09	18SEP09	261d	Rapid Set PCC QCP																																			
1230	Bridge Removal Plan Development		20d	20d	21AUG09	18SEP09	283d	Bridge Removal Plan Development																																			
1310	Survey Cross Sections of Earthwork Areas bef Gra		20d	20d	21AUG09	18SEP09	28d	Survey Cross Sections of Earthwork Areas bef Gra																																			
1730	Flow Control Structure Materials		20d	20d	21AUG09	18SEP09	233d	Flow Control Structure Materials																																			
1165	Pile Driving Plan Submittal		25d	25d	21AUG09	25SEP09	310d	Pile Driving Plan Submittal																																			
1150	Precast Quality Control Plan Girders		30d	30d	21AUG09	02OCT09	104d	Precast Quality Control Plan Girders																																			
1160	Precast Quality Control Plan Piles		30d	30d	21AUG09	02OCT09	56d	Precast Quality Control Plan Piles																																			
1170	Develop falsework Plans Adobe Reyes Bridge		30d	30d	21AUG09	02OCT09	274d	Develop falsework Plans Adobe Reyes Bridge																																			
<b>24AUG09</b>																																											
1050	Review and Approve SWPPP		20d	20d	28AUG09	25SEP09	10d	Review and Approve SWPPP																																			
<b>31AUG09</b>																																											
1030	CPM schedule Approval		11d	11d	02SEP09	17SEP09	16d	CPM schedule Approval																																			
1280	Lead Excavation and Transport Plan Approval		6d	6d	03SEP09	11SEP09	147d	Lead Excavation and Transport Plan Approval																																			
1260	Lead Compliance Plan Approval		8d	8d	04SEP09	16SEP09	144d	Lead Compliance Plan Approval																																			
<b>21SEP09</b>																																											
1240	Bridge Removal Plan Approval		7d	7d	21SEP09	29SEP09	283d	Bridge Removal Plan Approval																																			
1110	Review of communications routing Material		10d	10d	21SEP09	02OCT09	5d	Review of communications routing Material																																			
1125	Sign Panel Quality Control Plan Review		10d	10d	21SEP09	02OCT09	282d	Sign Panel Quality Control Plan Review																																			
1320	Prepare Sign Structure Shop Drawings		20d	20d	21SEP09	16OCT09	257d	Prepare Sign Structure Shop Drawings																																			
1740	Electroliers		70d	70d	21SEP09	30DEC09	193d	Electroliers																																			
<b>28SEP09</b>																																											
1168	Pile Drive Plan Submittal Approval		15d	15d	28SEP09	16OCT09	310d	Pile Drive Plan Submittal Approval																																			
1300	Bridge Survey Data and Forescale (30d pri deck)		20d	20d	28SEP09	23OCT09	156d	Bridge Survey Data and Forescale (30d pri deck)																																			
<b>05OCT09</b>																																											
1015	Establish Office Within 20 days of NTP		3d	3d	05OCT09	07OCT09	0	Establish Office Within 20 days of NTP																																			
1180	Review Falsework Plans Adobe Reyes Bridge		20d	20d	05OCT09	30OCT09	274d	Review Falsework Plans Adobe Reyes Bridge																																			
1710	Fabricate Concrete Piles		30d	30d	05OCT09	16NOV09	56d	Fabricate Concrete Piles																																			
1700	Fabricate Concrete Girders		50d	50d	05OCT09	15DEC09	104d	Fabricate Concrete Girders																																			

Start date	28JUL09
Finish date	27JAN11
Data date	28JUL09
Run date	08OCT09
Page number	1A
© Primavera Systems, Inc.	

**Powell Constructors  
Baseline Caltrans Schedule  
Adobe Reyes Roa...**

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Progress point
- Critical point
- Summary point
- Start milestone point
- Finish milestone point

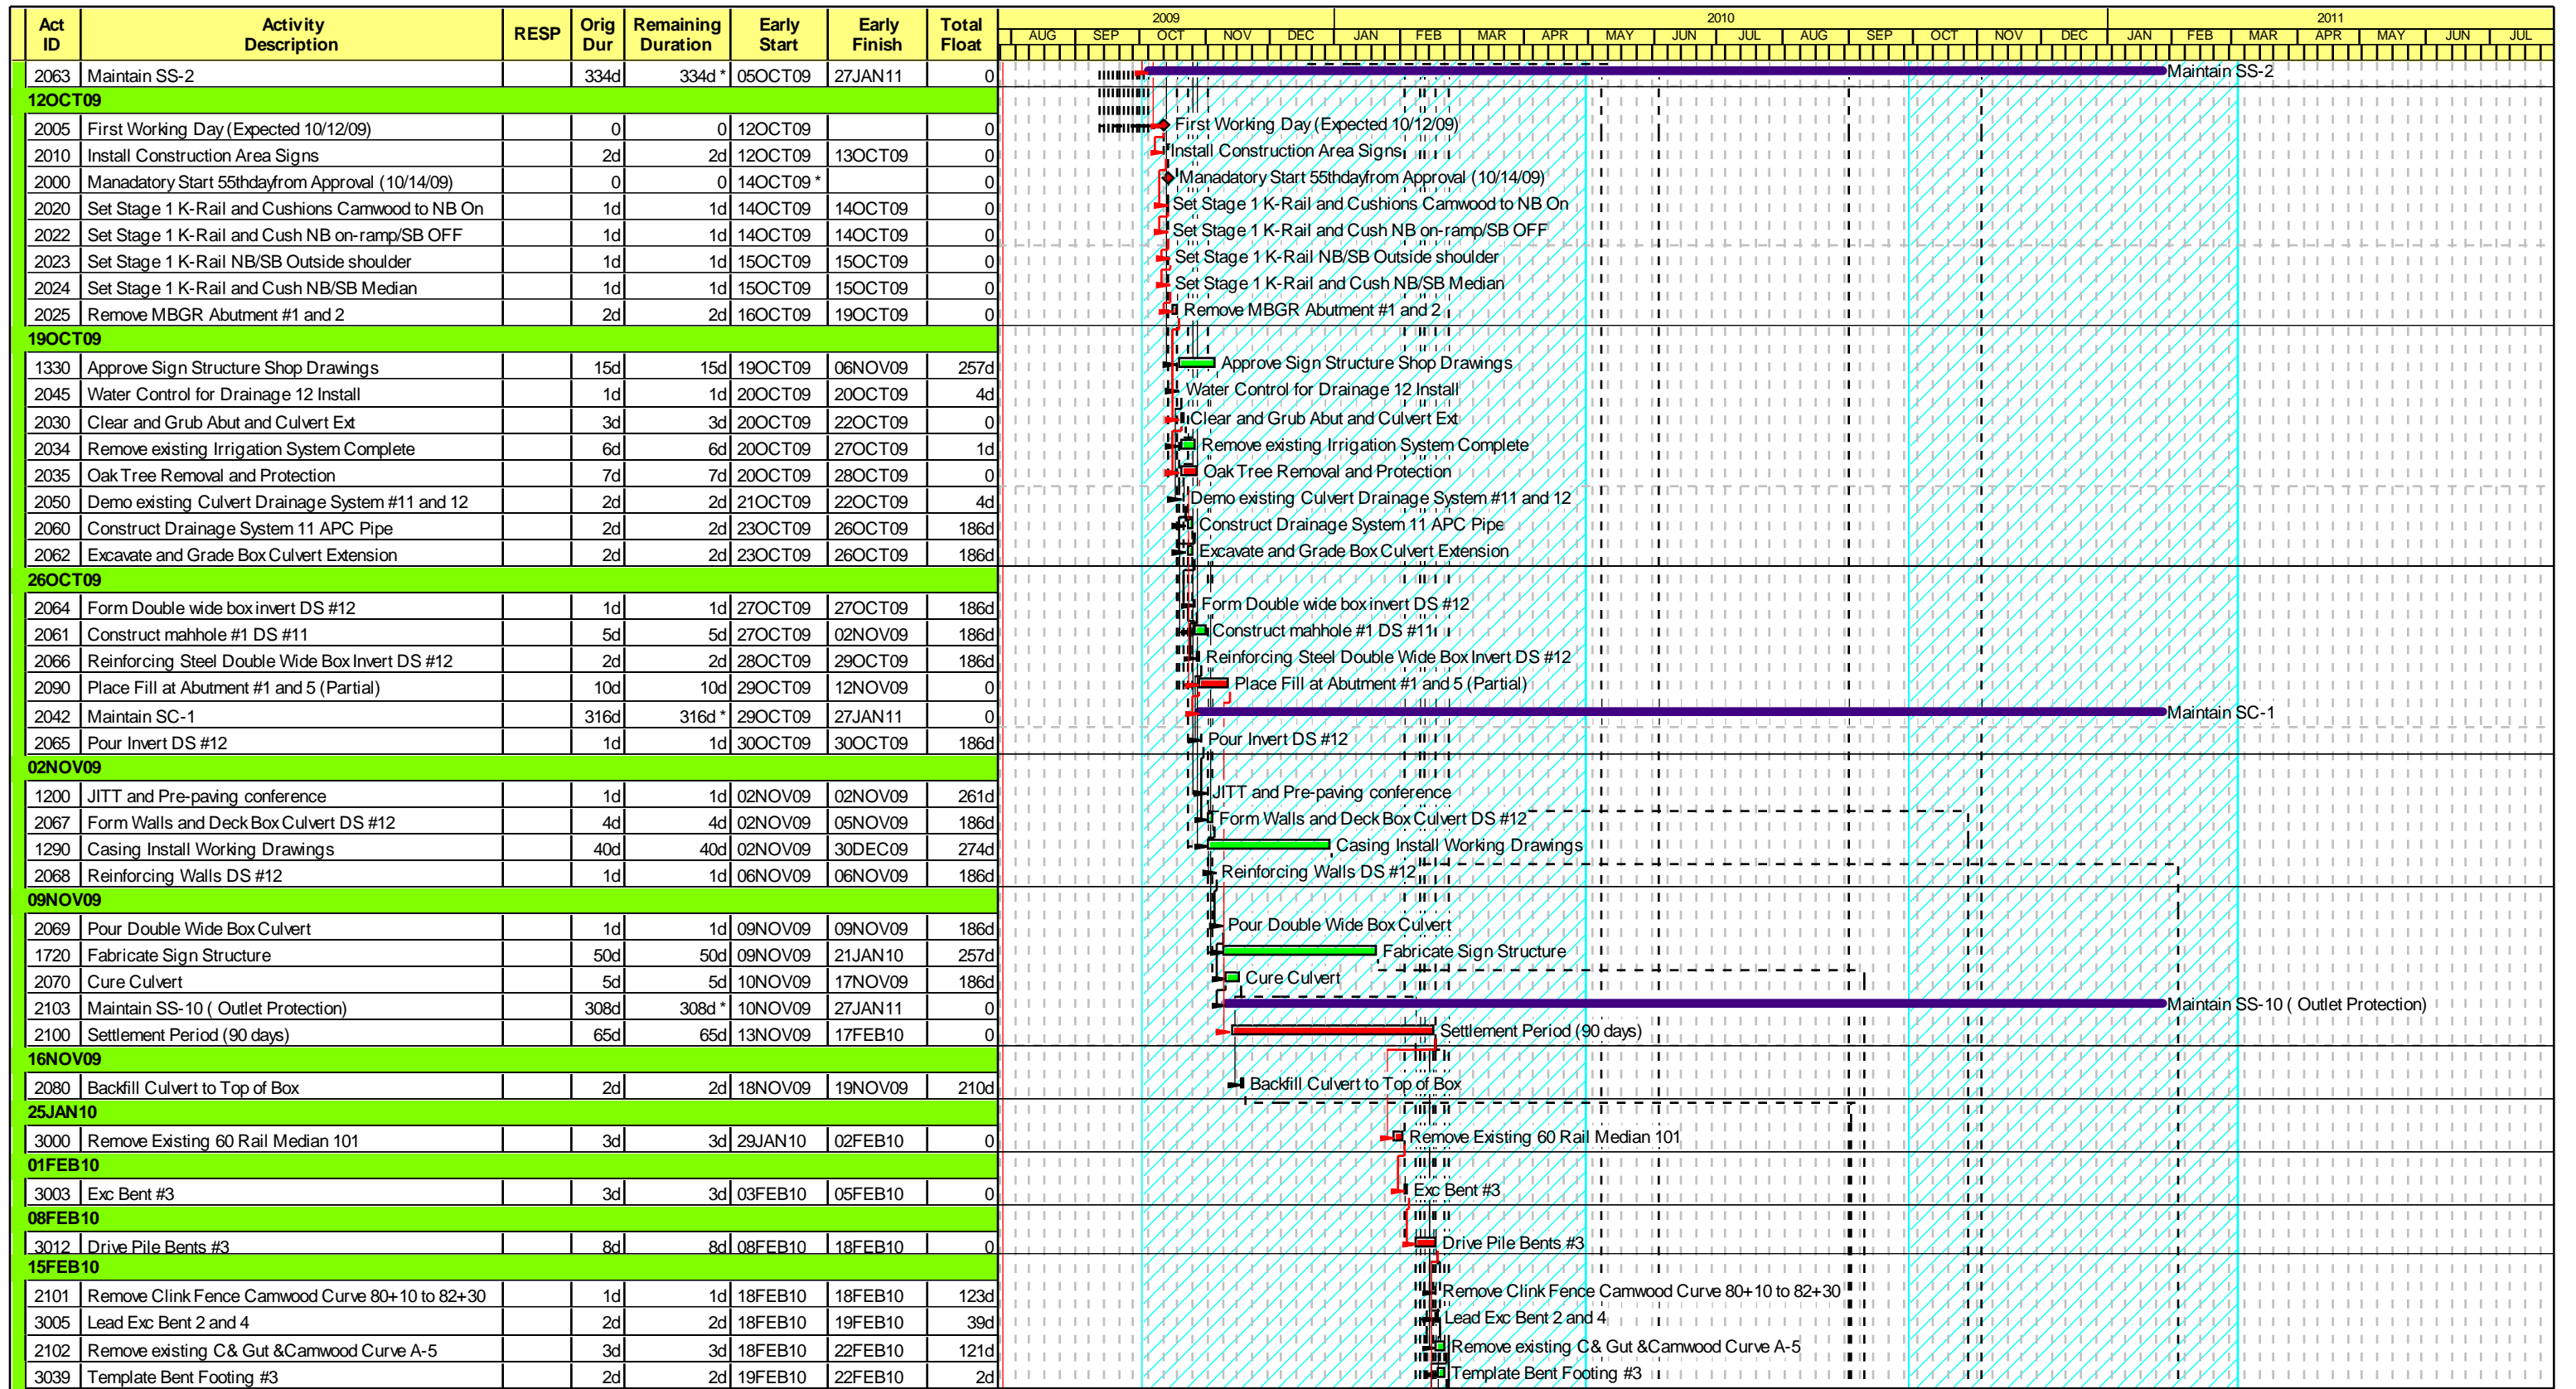

Start date 28JUL09  
 Finish date 27JAN11  
 Data date 28JUL09  
 Run date 08OCT09  
 Page number 2A

**Powell Constructors**  
**Baseline Caltrans Schedule**  
**Adobe Reyes Roa...**

- █ Early bar
- █ Progress bar
- █ Critical bar
- █ Summary bar
- ▲ Progress point
- ▲ Critical point
- ◆ Summary point
- ◆ Start milestone point
- ◆ Finish milestone point







