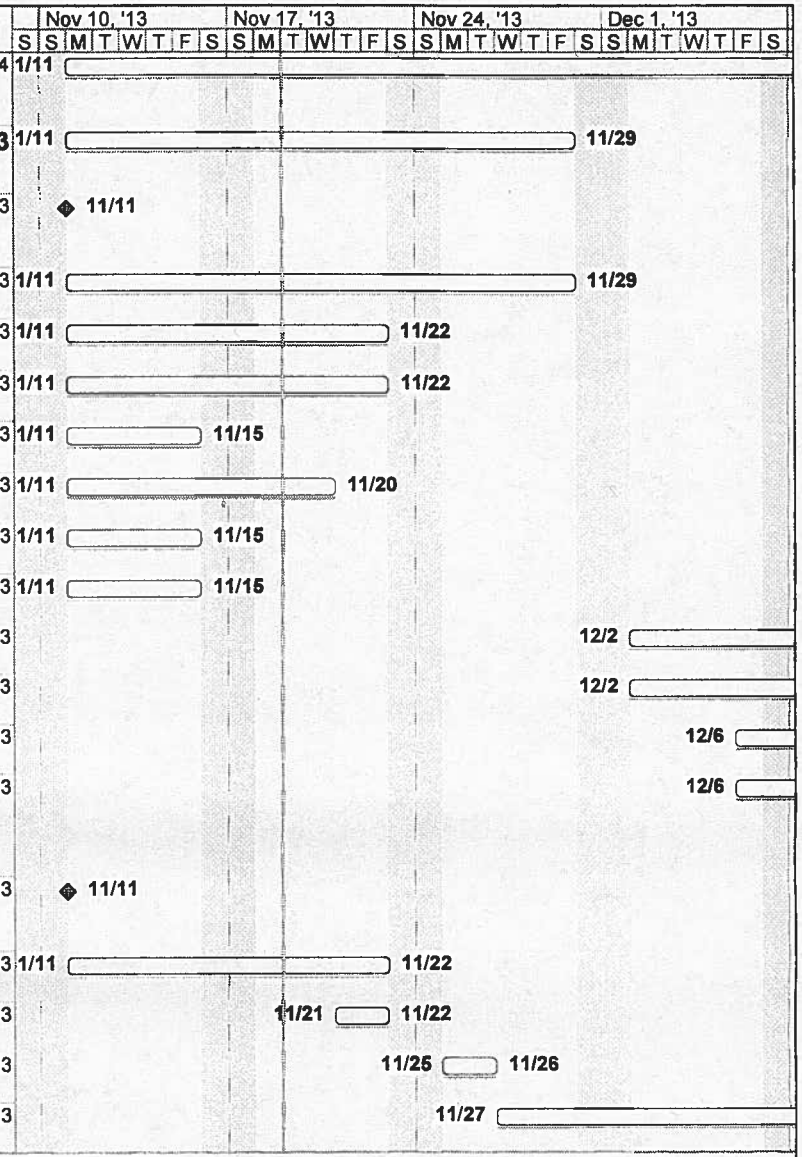ID	Task Name	Duration	Start	Finish
1	**Agoura Hills Recreation Center**	242 days	Mon 11/11/13	Tue 10/14/14
2	**2 Week Overview**	**15 days**	**Mon 11/11/13**	**Fri 11/29/13**
3	**Area B**	0 days	Mon 11/11/13	Mon 11/11/13
4	Selected Demolition	15 days	Mon 11/11/13	Fri 11/29/13
5	Electric Demolition	10 days	Mon 11/11/13	Fri 11/22/13
6	Elevator Demolition	10 days	Mon 11/11/13	Fri 11/22/13
7	Fire Alarm Demolition	5 days	Mon 11/11/13	Fri 11/15/13
8	Fire Sprinkler Demolition	8 days	Mon 11/11/13	Wed 11/20/13
9	HVAC Demolition	5 days	Mon 11/11/13	Fri 11/15/13
10	Plumbing Demolition	5 days	Mon 11/11/13	Fri 11/15/13
11	Footing Concrete	18 days	Mon 12/2/13	Wed 12/25/13
12	Electric Underground	7 days	Mon 12/2/13	Tue 12/10/13
13	Elevator Pit Concrete	7 days	Fri 12/6/13	Mon 12/16/13
14	Plumbing Underground	7 days	Fri 12/6/13	Mon 12/16/13
15				
16	**Area C**	0 days	Mon 11/11/13	Mon 11/11/13
17	Demolition & Grading	10 days	Mon 11/11/13	Fri 11/22/13
18	Survey	2 days	Thu 11/21/13	Fri 11/22/13
19	Bldg Lay-Out	2 days	Mon 11/25/13	Tue 11/26/13
20	Footing Concrete	16 days	Wed 11/27/13	Wed 12/18/13
